



Dashboard

All Tickets

Analytics

Knowledge Base

TICKETING SYSTEM



PROGRESS STATUS UPDATE


Phases	Activity	Status				
Phase 1: Discovery & Planning						
	Project Kickoff	Completed	100%			
	Research & Requirements Gathering	Completed	100%			
	Blueprint Diagram	Completed	100%			
	UI Framework Setup	Ongoing	80%			
Phase 2: Deployment (Build & Debug)						
	System Configuration	Ongoing	70%			
	User Account Setup	Ongoing	75%			
	Chat & Notification Setup	Ongoing	70%			
	SLA & Escalation Configuration	Ongoing	60%			
	User Acceptance Testing (Test Environment)	Not Started	0%			
	Issue Resolution	Not Started	0%			
Phase 3: Run & Monitor						
	System Go-Live	Not Started	0%			
	Ticket Monitoring	Not Started	0%			
	SLA Compliance Review	Not Started	0%			
	System Optimization	Not Started	0%			
	Project Completion	Not Started	0%			

Phases	%Completion
Discovery & Planning	95%
Deployment	45.83%
Run & Monitor	0.00%
Overall Progress:	46.94%



R2 Retrospective Updates: What went well?

- The **Blueprint Diagram** was successfully completed, ensuring proper ticket assignment settings for all departments and defining public and private ticket access.
- The **Analytics** downloadable files feature was implemented, enabling users to export system data and download pending ticket reports for monitoring.
- The **Admin Management** module for Admin (IT Users) was completed, including the functionality to add additional users to the system.
- The **User/Employee login** setup was successfully configured for all departments except Sales.
- The **Sales Department** button was finalized, allowing Sales users to create tickets through the “Sales Department” option without requiring a login.
- The **Knowledge Base (Help Center)** was implemented to support users with guidance and documentation.
- The **Notification** System was implemented to keep users informed about ticket updates, responses, and status changes.



R2 Retrospective Updates: What went wrong?

- **UI (User Interface)** – Some labels, dropdown options, and field indicators were inconsistent and needed updates for better clarity and usability.
- **Validation** – Some required fields and input checks were not fully enforced and still needed to be reviewed and tested.
- **Chats** – Chat messages appear longer than expected.
- **Bugs** – Minor system issues were found, such as dropdown errors and attachment problems, which required fixes.




R2 Retrospective Updates: Agile Action Registry

- **Finalize SLA Configuration** – Set the ticket response time and escalation rules.
- **Improve UI Consistency** – Align dropdowns, labels, required fields, and apply the system theme.
- **Implement Notification System** – Enable alerts for ticket updates and status changes.
- **Enhance Chat and Notes Feature** – Improve communication within tickets.
- **Conduct System Testing and Bug Fixing** – Test the system and resolve errors.
- **Prepare for System Go-Live** – Finalize setup and prepare the system for deployment.

R2:

BLUEPRINT DIAGRAM

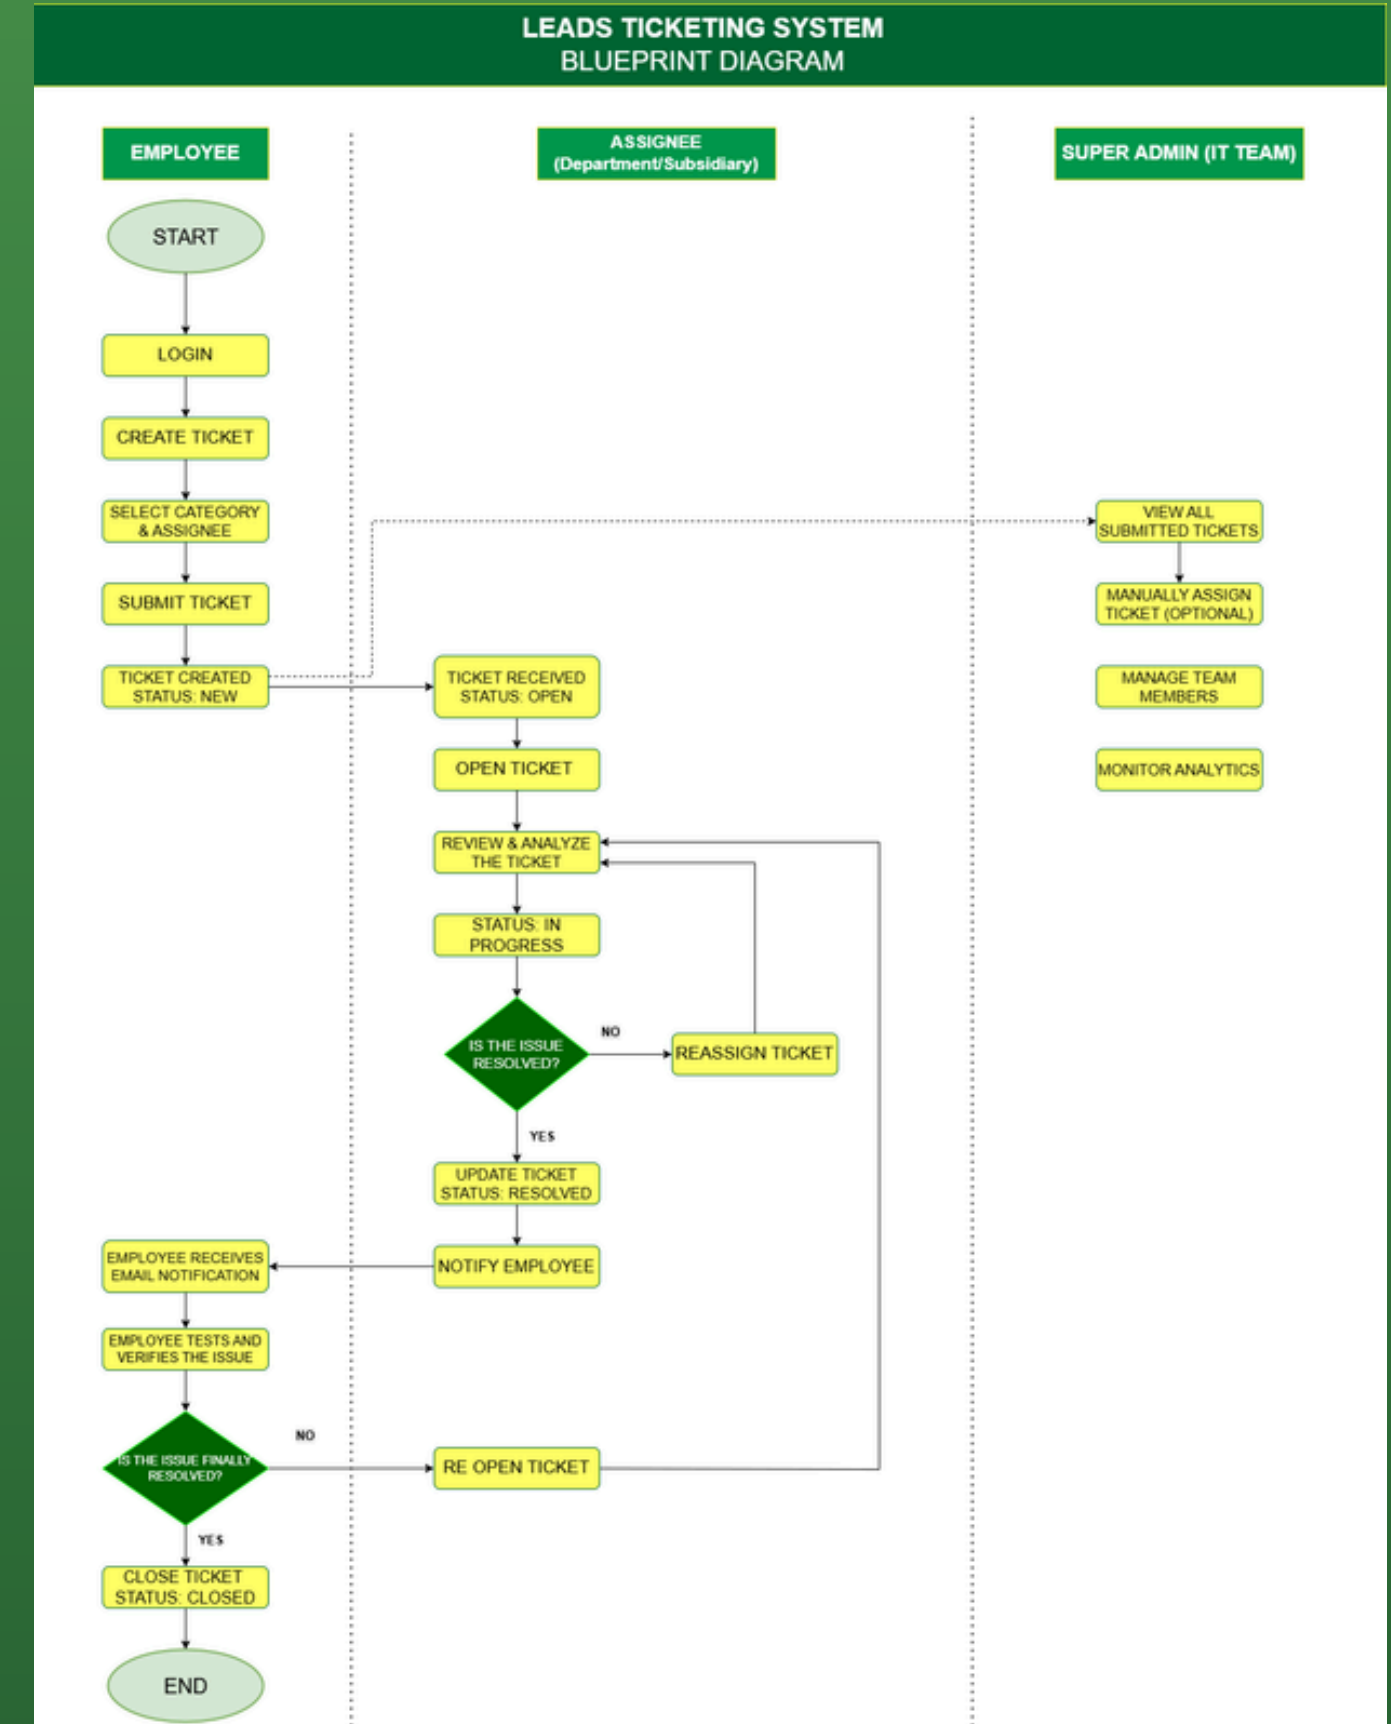



Angelica Herrera



Rachelle Ann
Ambayan



Enzo Charles
Mendoza



Matthew Alexis
Pascua

Meet Our Team
